Project Human Resource Management

by:
Benilda Eleonor V. Comendador, DIT

Project Human Resource Management

- the processes that organize, manage, and lead the project team.

Project Human Resource Management Processes

- **Plan Human Resource Management**

  - identifying and documenting project roles, responsibilities, and reporting relationships.

- **Acquire Project Team**

  - confirming human resource availability and obtaining the team necessary to complete project activities.

- **Develop Project Team**

  - improving competencies, team member interaction, and overall team environment to enhance project performance.

- **Manage Project Team**

  - Tracking team member performance, providing feedback, resolving issues, and managing changes.

Project Human Resource Management Overview

Plan Human Resource Management

.1 Input
- .1 Project management plan
- .2 Activity resource requirements
- .3 Enterprise environmental factors
- .4 Organizational process assets

.2 Tools & Techniques
- .1 Organizational charts and position descriptions
- .2 Networking
- .3 Organizational theory
- .4 Expert judgment
- .5 Meetings

.3 Outputs
- .1 Human resource management plan

Acquire Project Team

.1 Input
- .1 Human resource management plan
- .2 Enterprise environmental factors
- .3 Organizational process assets

.2 Tools & Techniques
- .1 Pre-assignment
- .2 Negotiation
- .3 Acquisition
- .4 Virtual teams
- .5 Multi-criteria decision analysis

.3 Outputs
- .1 Project staff assignments
- .2 Resource calendars
- .3 Project management plan updates

Develop Project Team

.1 Input
- .1 Human resource management plan
- .2 Project staff assignments
- .3 Resource calendars

.2 Tools & Techniques
- .1 Interpersonal skills
- .2 Training
- .3 Team-building activities
- .4 Ground rules
- .5 Colocation
- .6 Recognition and rewards
- .7 Personnel assessment tools

.3 Outputs
- .1 Team performance assessments
- .2 Enterprise environmental factors updates

Manage Project Team

.1 Input
- .1 Human resource management
- .2 Project staff assignments
- .3 Team performance assessments
- .4 Issue log
- .5 Work performance reports
- .6 Organizational process assets

.2 Tools & Techniques
- .1 Observation and conversation
- .2 Project performance appraisals
- .3 Conflict management
- .4 Interpersonal skills

.3 Outputs
- .1 Change requests
- .2 Project management plan updates
- .3 Project documents updates
- .4 Enterprise environmental factors updates
- .5 Organizational process assets updates

Plan Human Resource Management: Inputs, Tools & Techniques, and Outputs

Inputs	Tools & Techniques	Outputs
.1 Project management plan .2 Activity resource requirements .3 Enterprise environmental factors .4 Organizational process assets	.1 Organizational charts and position descriptions .2 Networking .3 Organizational theory .4 Expert judgment .5 Meetings	.1 Human resource management plan

Plan Human Resource Management Data Flow Diagram

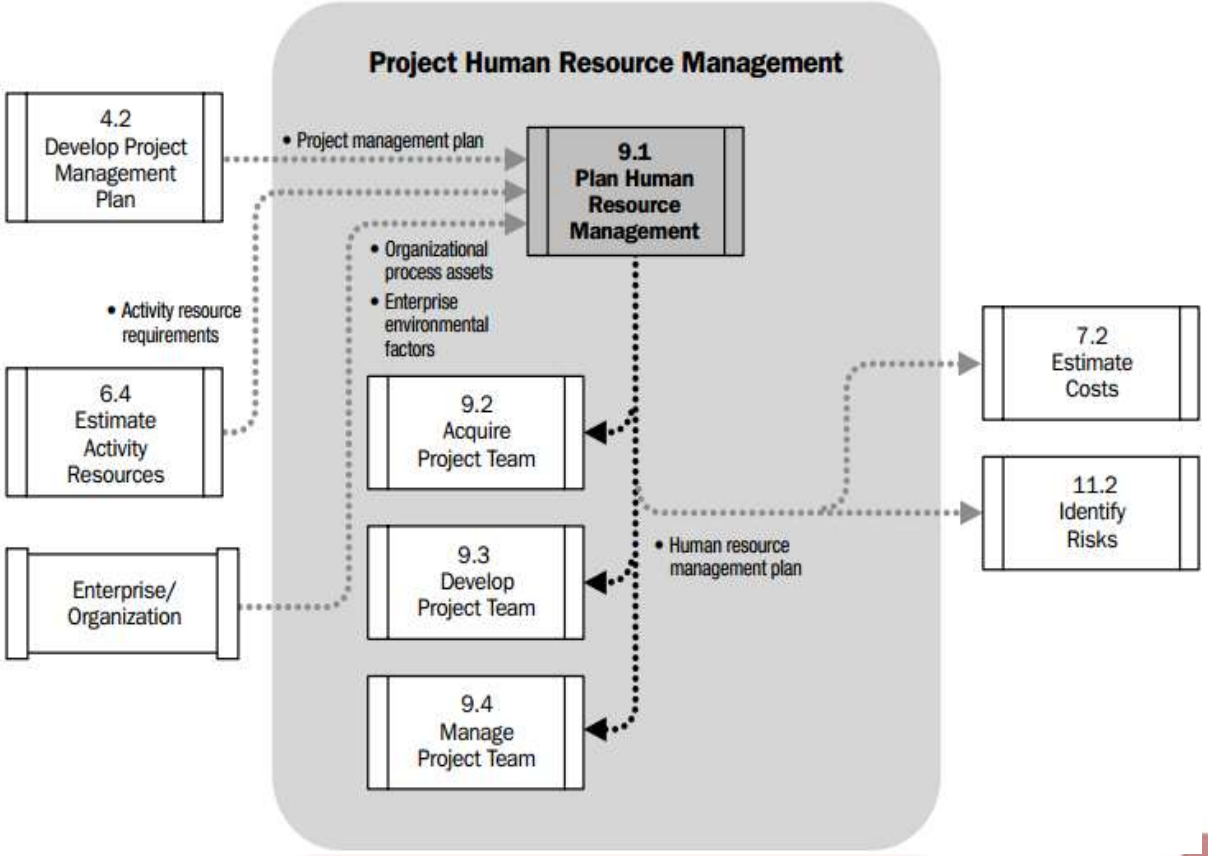

Roles and Responsibility Definition Formats

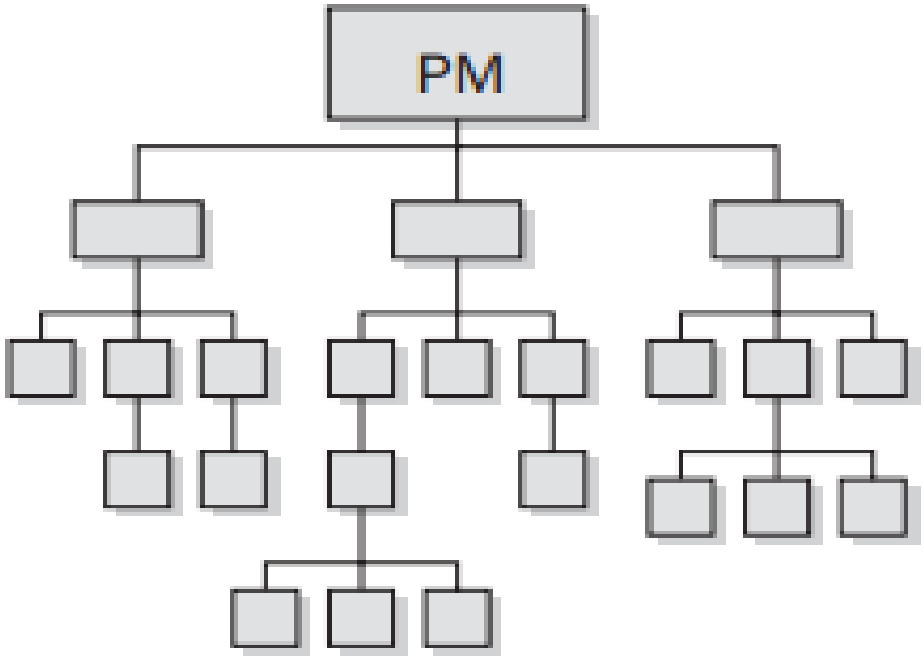

Organization Chart (hierarchical)

Roles and Responsibility Definition Formats

- Hierarchical-type chart

  - The traditional organizational chart structure can be used to show positions and relationships in a graphical, top-down format.

Roles and Responsibility Definition Formats

RAM				

Responsibility Chart (matrix)

Roles and Responsibility Definition Formats

- Matrix-based charts

  - A responsibility assignment matrix is a grid that shows the project resources assigned to each work package.

Ex. RACI (responsible, accountable, consult, and inform)

Roles and Responsibility Definition Formats

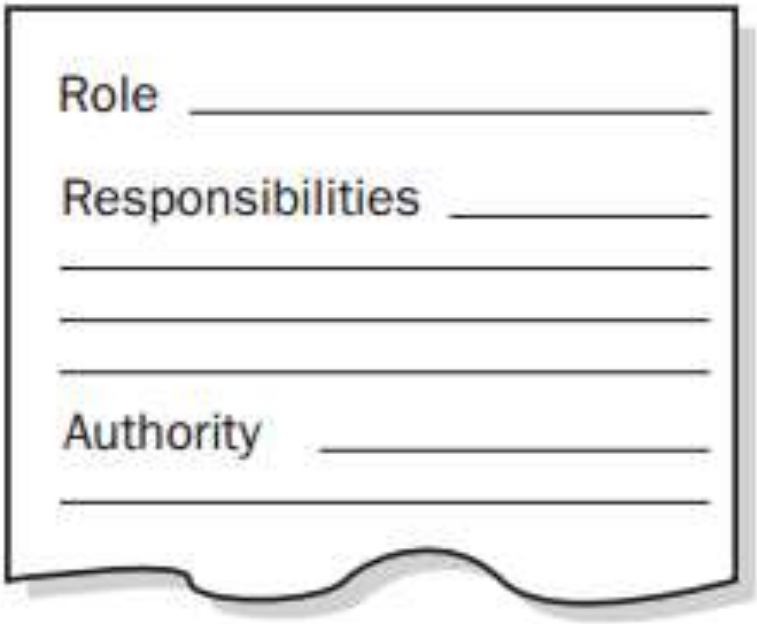

Role Description (text)

Roles and Responsibility Definition Formats

- Text-oriented formats

  - Team member responsibilities that require detailed descriptions can be specified in text-oriented formats.

Staffing Management Plan

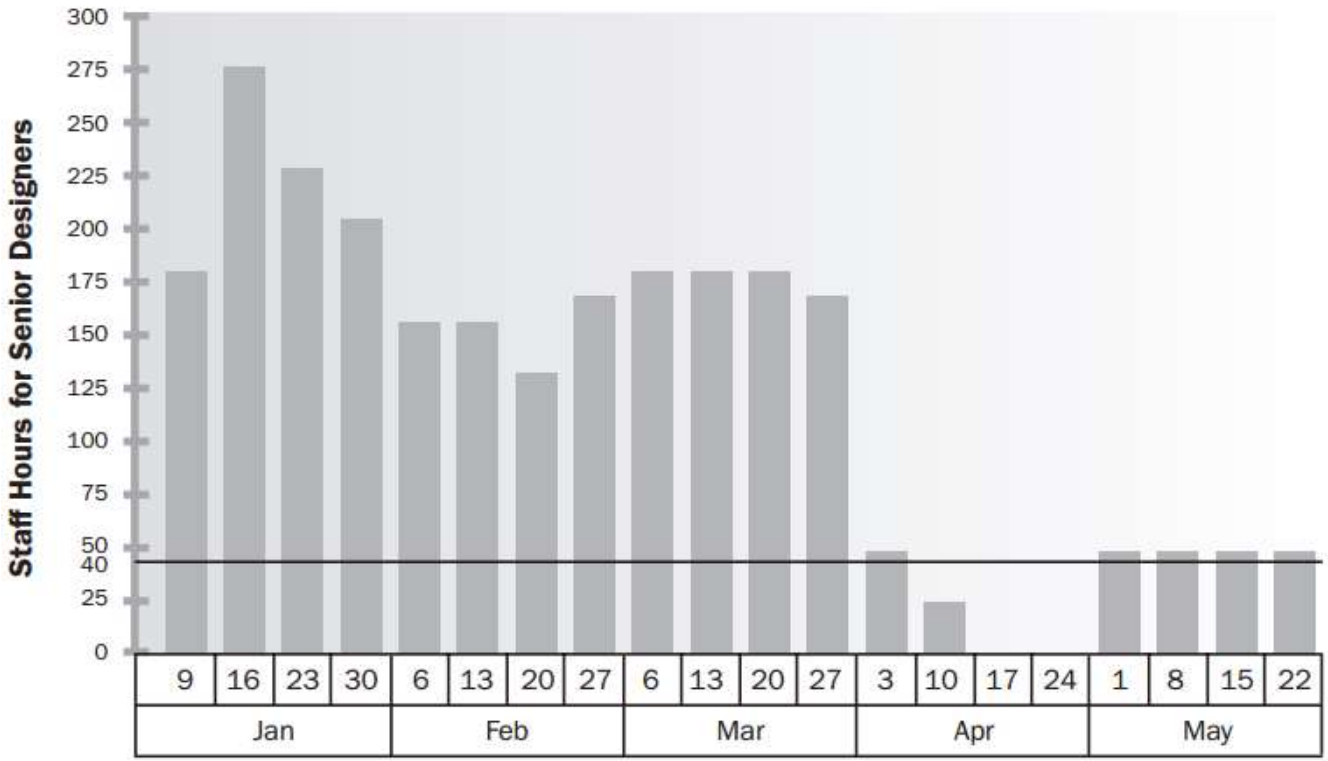

Resource Histogram

Acquire Project Team: Inputs, Tools & Techniques, and Outputs

Inputs	Tools & Techniques	Outputs
.1 Human resource management plan .2 Enterprise environmental factors .3 Organizational process assets	.1 Pre-assignment .2 Negotiation .3 Acquisition .4 Virtual teams .5 Multi-criteria decision analysis	.1 Project staff assignments .2 Resource calendars .3 Project management plan updates

Acquire Project Team Data Flow Diagram

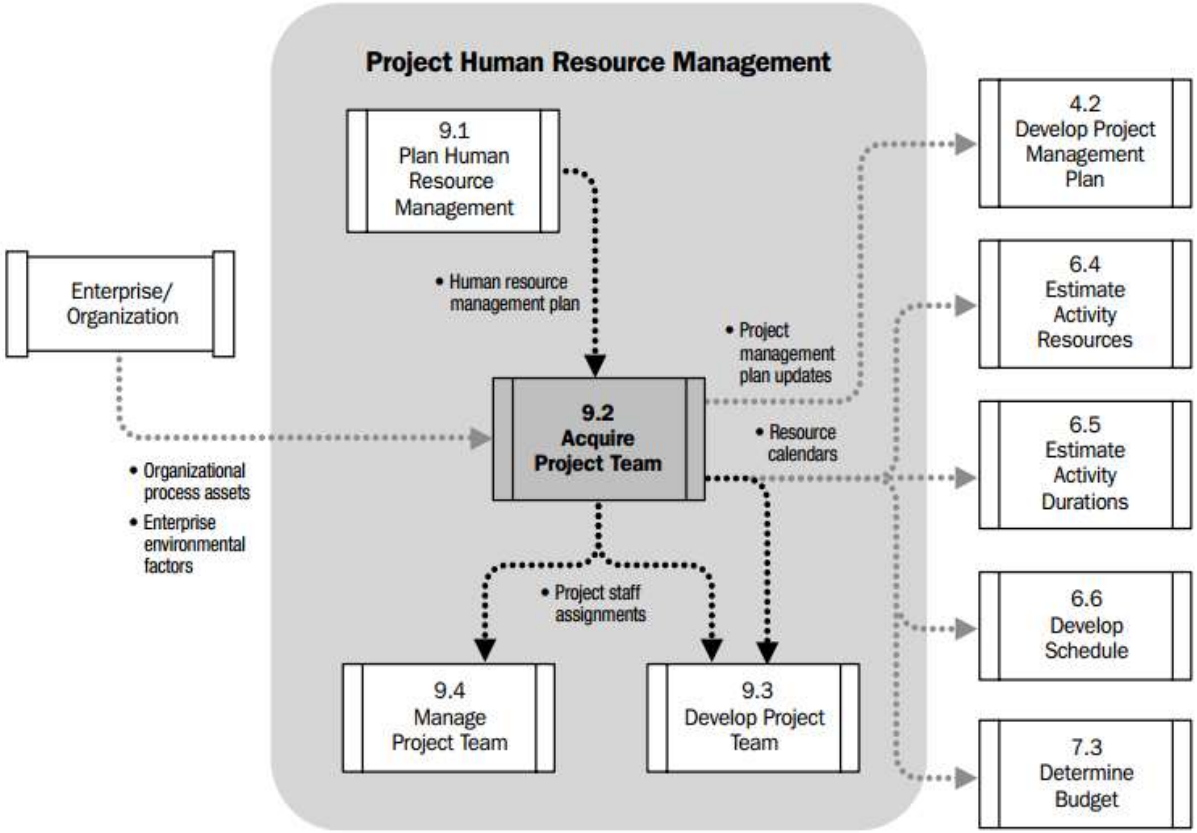

Manage Project Team: Inputs, Tools & Techniques, and Outputs

Inputs	Tools & Techniques	Outputs
1 Human resource management plan .2 Project staff assignments .3 Team performance assessments .4 Issue log .5 Work performance reports .6 Organizational process assets	.1 Observation and conversation .2 Project performance appraisal .3 Conflict management .4 Interpersonal skills	.1 Change requests .2 Project management plan updates .3 Project documents updates .4 Enterprise environmental factors updates .5 Organizational process assets updates

Manage Project Team Data Flow Diagram

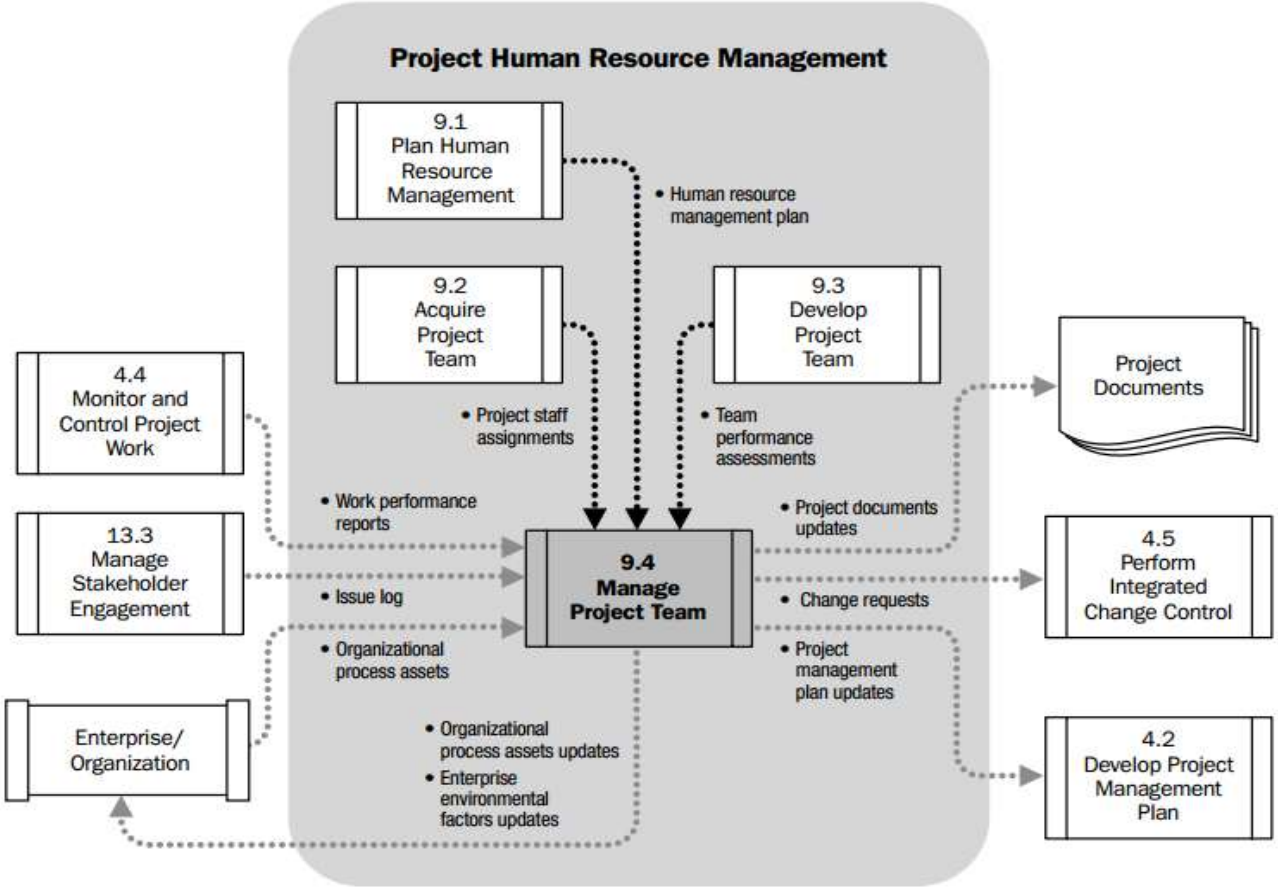

Thank you for your Attention !

Q and A
